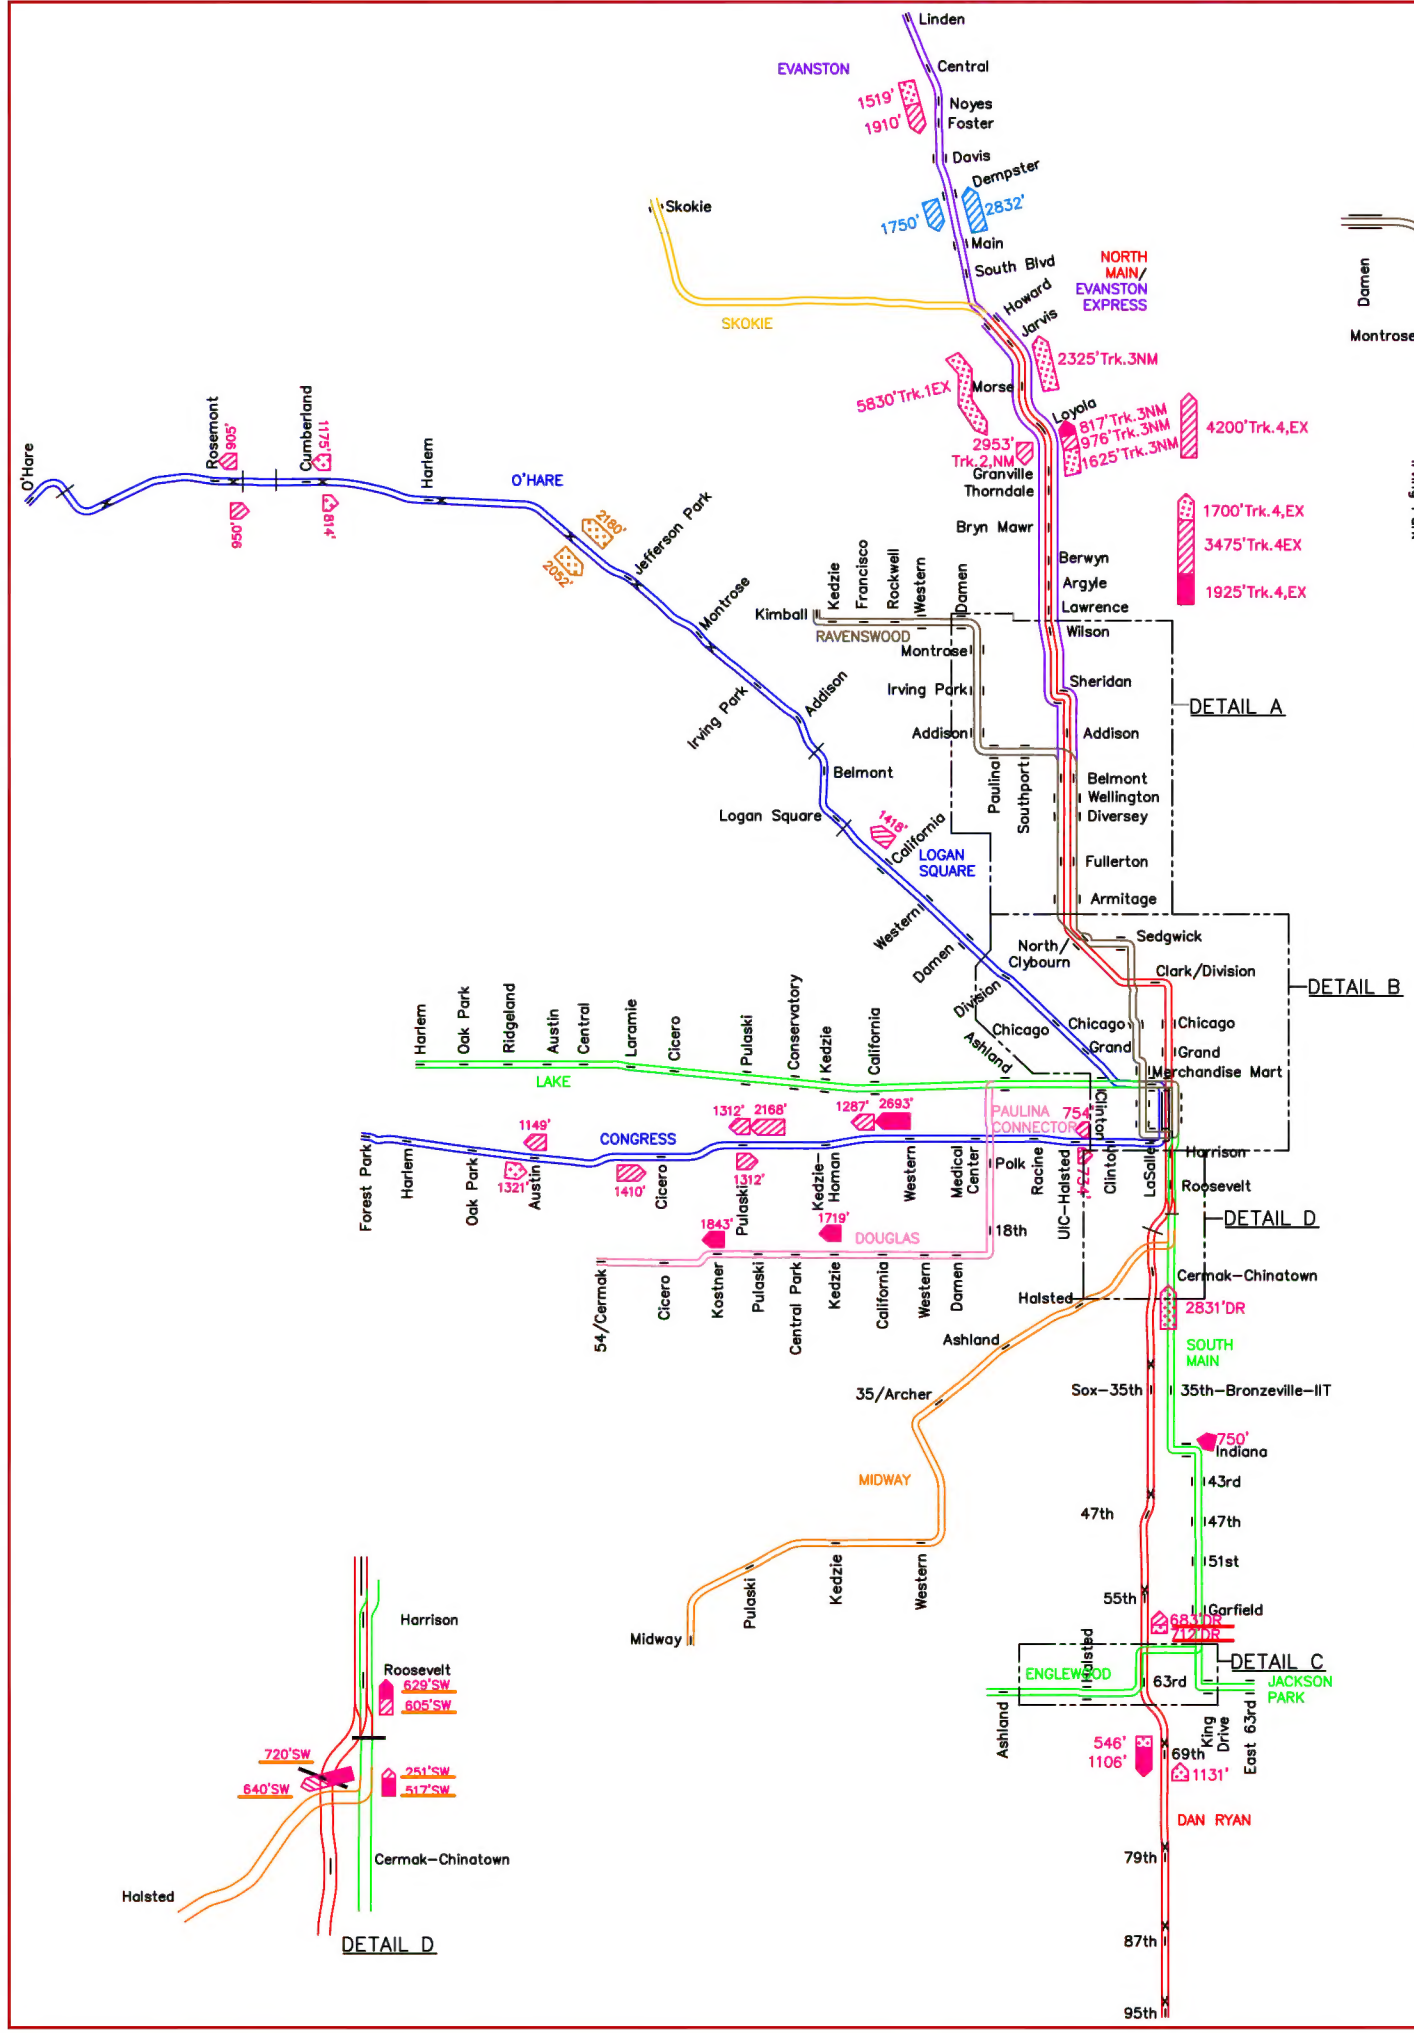

SLOW ZONE BY AREA				
Track (CTA)	15 mph	22,884	81,660	
	25 mph	39,334		
	35 mph	19,442		
Structure (CTA)	15 mph	0	4,582	
	25 mph	4,582		
	35 mph	0		
Signal (CTA)	15 mph	0	5,270	
	25 mph	0		
	35 mph	5,270		
Power (CTA)	15 mph	0	0	
	25 mph	0		
	35 mph	0		
Construction (CTA/Contractor)	15 mph	14,794	16,658	
	25 mph	0		
	35 mph	1,864		

★ NOTE: SIGNAL ISSUE RESULTING IN MULTIPLE 10 MIN. PLUS DELAYS DURING PREVIOUS MONTH

TOTAL SLOW ZONE TRACK

Rail Line	15 mph	25 mph	35 mph	Total Slow Zone	Linear Trk.–Ft.	% Slow	Movement Removed	Movement Added	Total SZ	% Slow
Congress	4,103	10,126	1,321	15,550	94,010	16.5	4,212	8,315	43,580	14.9
O'Hare/Logan Square	0	3,273	7,259	10,532	152,956	6.9	0	0		
Dearborn Subway	14,794	2,704	0	17,498	45,818	38.2	1,677	2,677		
North Main Line	3,275	6,178	2,875	12,328	78,966	15.6	670	0	19,337	8.3
State Subway	0	0	0	0	51,328	0	0	0		
Dan Ryan	1,106	683	5,220	7,009	101,332	6.9	0	0		
Skokie	0	0	0	0	52,146	0	0	0	0	0
Evanston	0	6,492	1,519	8,011	40,714	19.7	0	0	26,891	26.4
Evanston Express	3,675	7,675	7,530	18,880	60,970	31.0	0	0		
Loop	0	0	0	0	21,470	0	0	0	0	0
Ravenswood/Ravenswood–Loop	1,481	0	0	1,481	98,364	1.5	1,864	0	1,481	1.5
Midway/Grand Junction	1,877	251	0	2,128	99,224	2.1	0	0	2,128	2.1
Lake	0	0	0	0	93,114	0	0	0	11,191	5.4
South Loop/South Main Line	1,379	605	0	1,984	68,906	2.9	0	0		
Englewood	2,426	5,929	852	9,207	31,916	28.8	0	0		
Jackson Park	0	0	0	0	12,162	0	0	0		
Douglas/Paulina Connector	3,562	0	0	3,562	77,710	4.6	0	3,562	3,562	5.0
TOTALS	37,678	43,916	26,576	108,170	1,181,106	9.2	7,753	14,554		

NOT TO SCALE
GRAPHICAL REPRESENTATION

DATE	DESCRIPTION	
		IN CHARGE C.B.
		APPROVED BY B.M.jr
		CHECKED BY B.M.jr
		UPDATED BY S.M.
16 MAY 06	ORIGINAL	ORIGINATED BY J.J.H.
		Prepared by: Track Maintenance

CTA RAIL CUSTOMER IMPACT MAP

July 07, 2009
